Ecotech
ACOEM Group

Accredited for compliance with ISO/IEC 17025- Testing

Accreditation No. 14184.

NATA
WORLD RECOGNISED ACCREDITATION

WestConnex

M4 East Project

Ambient Air Quality and Weather Monitoring

Validated Report

1st November 2018 – 30th November 2018

Report No.: DAT14018 Rev1

Report issue date: 4th June 2019

Maintenance contract: MC2148

ECOTECH PTY LTD. ABN: 32005752081

1492 Ferntree Gully Rd, Knoxfield VIC. 3180. AUSTRALIA

Tel No: 1300 364 946 Fax No: 1300 668 763

Email ecotech@ecotech.com WEB www.ecotech.com

This document shall not be reproduced except for in full, without the written approval of Ecotech Pty Ltd.

Customer Details	
Customer	CPB Samsung John Holland Joint Venture
Contact name	Will Benson
Address	L2, 52 Railway Parade, Burwood, NSW 2134

Revision History			
Revision	**Report ID**	**Date**	**Analyst**
0	DAT14018	14/12/2018	Adriana Alvarez
1	DAT14018	04/06/2019	Adriana Alvarez

Refer to Appendix 3 for details of any amendments.

Report by: Adriana Alvarez

Approved Signatory: Jon Alexander

Table of Contents

Customer Details 2

Revision History 2

Table of Contents 3

List of Figures 4

List of Tables 5

Executive Summary 7

1.0 Introduction 8

2.0 Monitoring and Data Collection 8

2.1. Siting Details 8

2.2. Monitored Parameters 10

2.3. Data Collection Methods 11

2.3.1. Data Acquisition 13

2.4. Data Validation and Reporting 13

2.4.1. Validation 13

2.4.2. Reporting 13

3.0 Air Quality Goals 15

4.0 Calibrations and Maintenance 17

4.1. Units and Uncertainties 17

4.2. Maintenance 18

4.2.1. Calibration & Maintenance Summary Tables 18

5.0 Results 24

5.1. Data Capture 24

5.2. Air Quality Monthly Summary 26

5.3. Tabulated data 32

5.3.1. Annual average 32

5.4. Graphic Representations 34

6.0 Valid Data Exception Tables 44

7.0 Report Summary 52

Appendix 1 - Definitions & Abbreviations 53

Appendix 2 - Explanation of Exception Table 55

Appendix 3 - Amendments 57

List of Figures

Figure 1: M4 East Project Monitoring Station Locations 9

Figure 2: M4 East Project Air Monitoring Stations - CO 8 hours Rolling graph for November 2018 34

Figure 3: M4 East Project Air Monitoring Stations - NO_2 graph for November 2018 35

Figure 4: M4 East Project Air Monitoring Stations - PM_{10} 24 Hour graph for November 2018 36

Figure 5: M4 East Project Air Monitoring Stations - $PM_{2.5}$ 24 Hour graph November 2018 37

Figure 6: Allen Street – Wind Rose for November 2018 38

Figure 7: Concord Oval – Wind Rose for November 2018 39

Figure 8: Haberfield Public School – Wind Rose for November 2018 40

Figure 9: Powells Creek – Wind Rose for November 2018 41

Figure 10: Ramsay Street – Wind Rose for November 2018 42

Figure 11: Saint Lukes Park – Wind Rose for November 2018 43

List of Tables

Table 1: WestConnex M4 NSW East Project monitoring sites locations 8

Table 2: Parameters measured at the M4 East Project monitoring stations 10

Table 3: Methods 11

Table 4: M4 East Project - Air Quality Goals 15

Table 5: Units and Uncertainties 17

Table 6: M4 East Project Allen Street Maintenance Table November 2018 19

Table 7: M4 East Project Concord Oval Maintenance Table November 2018 20

Table 8: M4 East Project Haberfield Public School Maintenance Table November 2018 21

Table 9: M4 East Project Powells Creek Maintenance Table November 2018 22

Table 10: M4 East Project Ramsay Street Maintenance Table November 2018 23

Table 11: M4 East Project Saint Lukes Park Maintenance Table November 2018 24

Table 12: Data Capture for M4 East Project Ambient Air Quality Network 25

Table 13: M4 East Project Allen Street Exceedences Recorded for November 2018 26

Table 14: M4 East Project Concord Oval Exceedences Recorded for November 2018 27

Table 15: M4 East Project Haberfield Public School Exceedences Recorded for November 2018 28

Table 16: M4 East Project Powells Creek Exceedences Recorded for November 2018 29

Table 17: M4 East Project Ramsay Street Exceedences Recorded for November 2018 30

Table 18: M4 East Project Saint Lukes Park Exceedences Recorded for November 2018 31

Table 19: 12 months to date averages of PM_{10} and $PM_{2.5}$ at the WestConnex M4 ambient air monitoring station 33

Table 20: Allen Street Valid Data Exception Table 44

Table 21: Concord Oval Valid Data Exception Table 46

Table 22: Haberfield Public School Valid Data Exception Table 47

Table 23: Powells Creek Valid Data Exception Table 49

Table 24: Ramsay Street Valid Data Exception Table 50

Table 25: Saint Lukes Park Valid Data Exception Table 51

Executive Summary

The M4 East project is a component of the WestConnex scheme, a NSW Government initiative to connect Sydney's west and south-west with the Sydney Airport and the Port Botany precinct. The project includes the widening of the existing M4 between Homebush Bay Drive and Underwood Road. Two new three-lane tunnels of approximately 5.5 km will extend from west of Pomeroy Street, Homebush to Alt Street at Haberfield. Interchanges or ramps will be upgraded or installed to allow access to/from the tunnel at the following locations: Homebush Bay Drive, Concord Road, Wattle Street and Parramatta Road at Ashfield/Haberfield. Tunnel ventilation facilities will be installed within the existing M4 road reserve near Underwood Road, Homebush and at the corner of Parramatta Road and Wattle Street at Haberfield. Operational ancillary facilities will be installed at Cintra Park. Associated road works, particularly at Parramatta Road to the M4 at Powells Creek and modification of the intersection of the existing M4 and Parramatta Road will also be undertaken as part of the works.

Ecotech Pty Ltd has been commissioned by CPB Samsung John Holland Joint Venture for air quality monitoring, data collection and reporting at six external ambient air quality monitoring stations: Allen Street AQM (Air Quality Monitoring), Powells Creek AQM, St Lukes Park AQM, Concord Oval AQM, Ramsay Street AQM and Haberfield Public School AQM.

1.0 Introduction

Ecotech Pty Ltd was commissioned by CPB Samsung John Holland Joint Venture to provide monitoring and data reporting for the M4 East Project ambient air quality and weather monitoring network, located as detailed in Table 1. Ecotech commenced data collection in December 2017.

This report presents the available data for November 2018.

The data presented in this report:

- Describes air quality measurements;
- Compares monitoring results;
- Has been quality assured;
- Complies with NATA accreditation requirements, where applicable.

2.0 Monitoring and Data Collection

2.1. Siting Details

The WestConnex M4 East Project monitoring network consists of six ambient air quality and weather monitoring stations. The stations location and siting details are described below.

Table 1: WestConnex M4 NSW East Project monitoring sites locations

Site Name	Geographical Coordinates	Height Above Sea Level (m)
Allen Street	33°51'44.21"S, 151° 5'9.79"E	3
Concord Oval	33°52'8.60"S, 151° 6'28.97"E	7
Haberfield Public School	33°52'45.70"S, 151° 8'4.01"E	26
Powells Creek	33°51'44.21"S, 151° 5'19.31"E	10
Ramsay Street	33°52'26.20"S, 151° 8'1.50"E	5
Saint Lukes Park	33°51'55.04"S, 151° 6'35.88"E	4

A siting audit to assess sites for compliance with *AS/NZS 3580.1.1:2016* has been completed as follows:

- Allen Street on 14/11/2018
- Concord Oval on 14/11/2018
- Haberfield Public School on 02/10/2018
- Powells Creek on 14/11/2018
- Ramsay Street on 02/10/2018
- Saint Lukes Park on 09/11/2018

Figure 1: M4 East Project Monitoring Station Locations

2.2. Monitored Parameters

Table 2 below details the parameters monitored and the instruments used at the M4 East Project monitoring stations. Appendix 1 defines any abbreviated parameter names used throughout the report.

Table 2: Parameters measured at the M4 East Project monitoring stations

Station(s)	Parameter Measured	Instrument and Measurement Technique	Elevation
Allen Street Concord Oval Haberfield Public School Powells Creek Ramsay Street Saint Lukes Park	CO	Ecotech Serinus 30 – NDIR gas filter correlation infrared photometry	2 m
	NO, NO_2, NO_x	Ecotech Serinus 40 – gas phase chemiluminescence	2 m
	$PM_{2.5}$	Met One BAM 1020 – Beta ray attenuation	2 m
	PM_{10}	Thermo – 1400 ab TEOM (Tapered Element Oscillating Microbalance)	2m
	Differential Temperature (elevation 2m)	Met One 062MP	2 m
	Differential Temperature (elevation 10m)	Met One 062MP	10 m
	Wind Speed (Horizontal, elevation 10m)	Gill Windsonic Op3	10 m
	Wind Direction (elevation 10m)	Gill Windsonic Op3	10 m
	Sigma	Calculation	-

2.3. Data Collection Methods

Table 3 below shows the methods used for data collection.

Table 3: Methods

Parameter Measured	Data Collection Methods Used	Description of Method
NO, NO_2, NO_x	AS/NZS 3580.5.1 - 2011	Methods for sampling and analysis of ambient air - Method 5.1: Determination of oxides of nitrogen-Chemiluminescence method
	Ecotech Laboratory Manual	In-house method 6.1 - Oxides of nitrogen by chemiluminescence
CO	AS/NZS 3580.7.1 - 2011	Methods for sampling and analysis of ambient air. Method 7.1: Determination of carbon monoxide—Direct-reading instrumental method
	Ecotech Laboratory Manual	In-house method 6.3 – Carbon monoxide by gas filter correlation spectrophotometry
PM_{10} (TEOM)	AS/NZ 3580.9.8-2008	Methods for sampling and analysis of ambient air. Method 9.8: Determination of suspended particulate matter - PM_{10} continuous direct mass method using a tapered element oscillating microbalance analyser.
	Ecotech Laboratory Manual	In-house method 7.3- Particulates - $PM_{2.5}$, PM_{10} by TEOM
$PM_{2.5}$ (BAM 1020)	AS/NZS 3580.9.12-2013[1]	Methods for sampling and analysis of ambient Air - Method 9.12: Determination of suspended particulate matter—$PM_{2.5}$ beta attenuation monitors
	Ecotech Laboratory Manual	In-house method 7.5 – Measurement of PM_{10}, $PM_{2.5}$ and TSP using Beta Attenuation Monitor
Vector Wind Speed (Horizontal)	AS 2923-1987[2]	Methods for sampling and analysis of ambient air. Method 14: Meteorological monitoring for ambient air quality monitoring applications

[1] As approved by the Department of Planning and Environment on 8th September 2017.

[2] Superseded by AS/NZ 3580.14 2014 but specifically referenced in ministerial conditions.

Parameter Measured	Data Collection Methods Used	Description of Method
	Ecotech Laboratory Manual	In-house method 8.1 - Wind speed (Horizontal) by anemometer
Vector Wind Direction	AS 2923-1987[3]	Methods for sampling and analysis of ambient air. Method 14: Meteorological monitoring for ambient air quality monitoring applications
	Ecotech Laboratory Manual	In-house method 8.3 - Wind direction by anemometer
Sigma	AS 2923-1987[3]	Methods of sampling and analysis of ambient air. Method 14: Meteorological monitoring for ambient air quality monitoring applications
	Ecotech Laboratory Manual	In-house method 8.3 Wind direction by anemometer
Atmospheric Temperature	USEPA (2000) EPA 454/R-99-005[3]	Methods for sampling and analysis of ambient air. Method 14: Meteorological monitoring for ambient air quality monitoring applications
	Ecotech Laboratory Manual	In-house method 8.4 – Temperature ambient by thermoelectric techniques

Note: Two different measurement techniques are used for monitoring PM_{10} and $PM_{2.5}$ at the M4 East Project Stations. Studies conducted in Canada, the United States and other countries have found that the Tapered Element Oscillating Microbalance (TEOM) monitors can under report concentrations compared to the Beta Attenuation Monitors (BAM), especially when the air contains a large proportion of semi-volatile particulate matter, which may be the case during cooler seasons when the air contains less coarse dust and a greater proportion of semi-volatile organic compounds such as those associated with wood smoke. As a result, it is normal to see occasional periods where $PM_{10} < PM_{2.5}$ and this situation does not necessarily indicate a fault with either instrument.

[3] Superseded by AS/NZ 3580.14 2014 but specifically referenced in ministerial conditions.

2.3.1. Data Acquisition

Data acquisition is performed using a PC based WinAQMS logger (using WinAQMS® Version 2.0) situated at each of the monitoring sites. Each logger is equipped with a 3G modem for remote data collection. The recorded data is remotely collected from the Air Quality Monitoring Station (AQMS) loggers on a daily basis (using Airodis™ version 5.1.0) and stored at Ecotech's Environmental Reporting Services (ERS) department in Melbourne, Australia. Data samples are logged in 5-minute intervals.

2.4. Data Validation and Reporting

2.4.1. Validation

The Ecotech ERS department performs daily data checks to ensure maximum data capture rates are maintained. Any equipment failures are communicated to the responsible field engineers for urgent rectification. Ecotech ERS maintains two distinct databases containing non-validated and validated data respectively.

The validated database is created by duplicating the non-validated database and then flagging data affected by instrument faults, calibrations and other maintenance activities. The data validation software requires the analyst to supply a valid reason (e.g. backed by maintenance notes, calibration sheets etc.) in the database for flagging any data as invalid.

Details of all invalid or missing data are recorded in the Valid Data Exception Tables.

Validation is performed by the analyst, and the validation is reviewed. Graphs and tables are generated based on the validated five minutes and one-hour data as appropriate.

2.4.2. Reporting

Data is reported in six Microsoft Excel format files named

- *WestConnex_M4_Allen St_ Monthly Data Report_ November 2018.xls*
- *WestConnex_M4_Concord Oval_ Monthly Data Report_ November 2018.xls*
- *WestConnex_M4_Haberfield School_ Monthly Data Report_ November 2018 Rev1.xls*
- *WestConnex_M4_Powells Creek_ Monthly Data Report_ November 2018.xls*
- *WestConnex_M4_Ramsay St_ Monthly Data Report_ November 2018.xls*
- *WestConnex_M4_St Lukes Park _Monthly Data Report_ November 2018.xls*

Each Excel file consists of 5 worksheets:

1. Cover
2. 5 Minute Data
3. 1 Hour Data
4. 24-hour Data
5. Valid Data Exception Report

The data contained in this report is based on Australian Eastern Standard Time.

All averages are calculated from the five-minute and the one-hour data. Averages are based on a minimum of 75% valid readings within the averaging period. Where data capture is low for a particular parameter, summary values (e.g. monthly maximum and minimum) may be based on less than 75% valid samples. The reader should use caution when interpreting these values as they may not be representative of conditions for the entire sample period.

Averaging periods of eight hours or less are reported for the end of the period, i.e. the hourly average 02:00am is for the data collected from 1:00am to 2:00am. One-hour averages are calculated based on a clock hour. One day averages are calculated based on calendar days.

3.0 Air Quality Goals

The air quality goals and criteria for pollutants monitored at the M4 East project ambient monitoring sites are based on SSI 6307 Planning Approval Condition E9. The air quality goals and criteria are shown in Table 4 below.

Table 4: M4 East Project - Air Quality Goals

Parameter	Time Period	Goal Level	Units
CO	8 hours (rolling, based on 1-hour averages)	9.0	ppm
NO_2	1 hour	0.12	ppm
PM_{10}	1 day	50	µg/m³
	1 year	25	µg/m³
$PM_{2.5}$	1 day	25	µg/m³
	1 year	8	µg/m³

Note:

Exceptional events are excluded from this standard. As per the Ambient Air Quality NEPM, ***Exceptional event*** means a fire or dust occurrence that adversely affects air quality at a particular location and causes an exceedance of 1-day average standards in excess of normal historical fluctuations and background levels and is directly related to: bushfire; jurisdiction authorized hazard reduction burning; or continental scale windblown dust.

Ecotech will include any valid data identified as being associated with an exceptional event in all report tables and graphic representations. For this reason, and as the project monitoring results are part of the baseline monitoring regime, 1-day averages associated with exceptional events will not be counted as exceedences of the Air Quality goals. Monitoring and reporting of exceedences during the operational project will be in accordance with the Planning Approval Conditions E10, E11 and E12.

There two exceedances of the air quality limits at the M4 East Westconnex Ambient Air Quality Monitoring Network for the reporting month. Please refer to Table 13-18 in Section 5.2 – Air Quality

Monthly Summary for further information. Ecotech have been advised that Sydney had experienced elevated particulate levels due to dust storms which may have had significant impact on reported particulate concentrations during 21st to 22nd November 2018.

4.0 Calibrations and Maintenance

4.1. Units and Uncertainties

The uncertainties for each parameter have been determined by the manufacturer's tolerance limits of the equipment's parameters, and by the data collection standard method.

The reported uncertainties are expanded uncertainties, calculated using coverage factors which give a level of confidence of approximately 95%.

Table 5: Units and Uncertainties

Parameter	Units	Resolution	Uncertainty	Measurement Range[4]
NO, NO_x (S40)	ppm	0.001 ppm	±1.3 ppm or 10% of reading, whichever is the greater k factor of 2.0	0 to 50 ppm
NO_2 (S40)	ppm	0.001 ppm	± 1.7 ppm k factor of 2.0	0 to 50 ppm
CO (S30)	ppm	0.1 ppm	± 1 ppm or 10% of reading, whichever is the greater k factor of 2.0	0 to 50 ppm
$PM_{2.5}$ (BAM1020)	µg/m³	1 µg/m³	±5.0 µg/m³ + 5.4% of reading K factor of 2.0	5 to 1000 µg/m³
PM_{10} (TEOM)	µg/m³	0.1 µg/m³	±5.0 µg/m³ or 3.6% of reading, whichever is the greater K factor of 2.0	0 µg/m³ to 1 g/m³
Vector Wind Speed	m/s	0.1 m/s	±0.4 m/s or 2 % of reading, whichever is greater K factor of 2.0	0 to 30 m/s
Vector Wind Direction	deg	1 deg	±4 deg K factor of 2.0	0 to 360 deg Starting threshold: 0 m/s

[4] Uncertainties may not be calculated based on the full measurement range.

Parameter	Units	Resolution	Uncertainty	Measurement Range[4]
Atmospheric Temperature	K	0.1 K	±0.6 K K factor of 2.0	273.15 to 323.15 K

4.2. Maintenance

4.2.1. Calibration & Maintenance Summary Tables

The last calibrations for the following parameters were performed on the indicated dates. Data supplied after this time is subject to further validation, to be performed at the next calibration cycle.

Note: Maintenance and calibration dates may differ, as calibrations may be less frequent than scheduled maintenance visits.

Tables 6-11 indicate when the particulate and gas and meteorological equipment were last maintained/calibrated.

Table 6: M4 East Project Allen Street Maintenance Table November 2018

Parameter	Date of Last Maintenance	Maintenance Type[5]	Date of Last Calibration	Calibration Cycle
NO, NO_2, NO_x	13/11/2018	Yearly	13/11/2018	Monthly
CO	13/11/2018	Yearly	13/11/2018	Monthly
PM_{10}	13/11/2018	Yearly	13/11/2018	6 Monthly
$PM_{2.5}$	13/11/2018	Yearly	13/11/2018	Yearly
WS/WD/Sigma	13/11/2018	Yearly	06/10/2017	2 yearly
Differential Temperature 2m	13/11/2018	Yearly	13/11/2018	6 Monthly
Differential Temperature 10m	13/11/2018	Yearly	13/11/2018	6 Monthly

[5] Additional visits may have been made as required

Table 7: M4 East Project Concord Oval Maintenance Table November 2018

Parameter	Date of Last Maintenance	Maintenance Type[6]	Date of Last Calibration	Calibration Cycle
NO, NO_2, NO_x	14/11/2018	Yearly	14/11/2018	Monthly
CO	14/11/2018	Yearly	14/11/2018	Monthly
PM_{10}	14/11/2018	Yearly	14/11/2018	6 Monthly
$PM_{2.5}$	14/11/2018	Yearly	14/11/2018	Yearly
WS/WD/Sigma	31/10/2018	Yearly	06/10/2017	2 yearly
Differential Temperature 2m	19/11/2018	Yearly	19/11/2018	6 Monthly
Differential Temperature 10m	19/11/2018	Yearly	19/11/2018	6 Monthly

[6] Additional visits may have been made as required.

Table 8: M4 East Project Haberfield Public School Maintenance Table November 2018

Parameter	Date of Last Maintenance	Maintenance Type[7]	Date of Last Calibration	Calibration Cycle
NO, NO_2, NO_x	07/11/2018	6 Monthly[8]	07/11/2018	Monthly
CO	07/11/2018	6 Monthly[9]	07/11/2018	Monthly
PM_{10}	09/11/2018	Yearly	09/11/2018	6 Monthly
$PM_{2.5}$	09/11/2018	Yearly	09/11/2018	Yearly
WS/WD/Sigma	30/10/2018	Yearly	05/10/2017	2 yearly
Differential Temperature 2m	19/11/2018	Yearly	19/11/2018	6 Monthly
Differential Temperature 10m	19/11/2018	Yearly	19/11/2018	6 Monthly

[7] Additional visits may have been made as required.

[8] Yearly maintenance was not due in November due to the instrument being installed in June 2018

[9] Yearly maintenance was not due in November due to the instrument being installed in February 2018

Table 9: M4 East Project Powells Creek Maintenance Table November 2018

Parameter	Date of Last Maintenance	Maintenance Type[10]	Date of Last Calibration	Calibration Cycle
NO, NO_2, NO_x	14/11/2018	Yearly	14/11/2018	Monthly
CO	14/11/2018	Yearly	14/11/2018	Monthly
PM_{10}	15/11/2018	Yearly	15/11/2018	6 Monthly
$PM_{2.5}$	15/11/2018	Yearly	15/11/2018	Yearly
WS/WD/Sigma	31/10/2018	Yearly	06/10/2017	2 yearly
Differential Temperature 2m	20/11/2018	Yearly	20/11/2018	6 Monthly
Differential Temperature 10m	20/11/2018	Yearly	20/11/2018	6 Monthly

[10] Additional visits may have been made as required.

Table 10: M4 East Project Ramsay Street Maintenance Table November 2018

Parameter	Date of Last Maintenance	Maintenance Type[11]	Date of Last Calibration	Calibration Cycle
NO, NO_2, NO_x	08/11/2018	Yearly	08/11/2018	Monthly
CO	08/11/2018	Yearly	08/11/2018	Monthly
PM_{10}	13/11/2018	Yearly	13/11/2018	6 Monthly
$PM_{2.5}$	12/11/2018	Yearly	12/11/2018	Yearly
WS/WD/Sigma	31/10/2018	Yearly	05/10/2017	2 yearly
Differential Temperature 2m	19/11/2018	Yearly	19/11/2018	6 Monthly
Differential Temperature 10m	19/11/2018	Yearly	19/11/2018	6 Monthly

[11] Additional visits may have been made as required.

Table 11: M4 East Project Saint Lukes Park Maintenance Table November 2018

Parameter	Date of Last Maintenance	Maintenance Type[12]	Date of Last Calibration	Calibration Cycle
NO, NO_2, NO_x	09/11/2018	Yearly	09/11/2018	Monthly
CO	12/11/2018	Monthly[13]	12/11/2018	Monthly
PM_{10}	09/11/2018	3 Monthly[14]	09/08/2018	6 Monthly
$PM_{2.5}$	12/11/2018	Yearly	12/11/2018	Yearly
WS/WD/Sigma	02/11/2018	Yearly	09/10/2017	2 yearly
Differential Temperature 2m	20/11/2018	Yearly	20/11/2018	6 Monthly
Differential Temperature 10m	20/11/2018	Yearly	20/11/2018	6 Monthly

5.0 Results

5.1. Data Capture

Valid data capture refers to the amount of valid data collected during the report period. It is based on 5-minute data, for gaseous and meteorological parameters and 1-hour data for particulate parameters.

The percentage of valid data captured is calculated using the following equation:

Valid Data capture = (Reported air quality data / Total data) x 100%

[12] Additional visits may have been made as required.

[13] Yearly maintenance was not due in November due to the instrument being installed in September 2018

[14] Yearly maintenance was not due in November due to the instrument being installed in February 2018

Where:

- Reported air quality data = Number of samples (instrument readings) which have been validated through a quality assured process and excludes all data errors, zero data collection due to calibration, equipment failures, planned and unplanned maintenance.
- Total data = Total number of samples (instrument readings) expected for the sampling period. Total data is calculated based on the same averaging period as "reported air quality data" and the duration of the corresponding report period. e.g. for 5-minute data collected over a month of 31 days, the total data would be equal to 12 (5-minute samples in an hour) x 24 (hours in a day) x 31 (days in a month) = 8928 samples.

Table 12 below displays data capture statistics for November 2018. **Bold** values in the table indicate data capture below 95%.

Details of all invalid or missing data affecting data capture are included in the Valid Data Exception Tables, see section 6.0.

Table 12: Data Capture for M4 East Project Ambient Air Quality Network

Parameter	Data Capture (%)					
	Allen Street	Concord Oval	Haberfield School	Powells Creek	Ramsay Street	Saint Lukes Park
$PM_{2.5}$	96.0	96.8	**23.4**	96.9	**87.9**	**88.9**
PM_{10}	95.8	96.6	94.4	96.8	**85.9**	97.7
CO	**94.2**	96.6	95.0	96.2	**94.5**	95.6
NO, NO_2, NO_x	**93.7**	96.9	94.7	97.1	95.2	95.5
WS, WD, Sigma	98.2	99.5	95.3	97.8	98.1	**88.9**
AT 2m	98.3	99.4	97.9	**94.9**	98.2	**88.7**
AT 10m	**57.3**	99.4	97.9	**94.9**	98.2	**88.7**

5.2. Air Quality Monthly Summary

Tables 13-18 below include a summary of any exceedances recorded at the M4 East Project stations during the reported period[15].

Table 13: M4 East Project Allen Street Exceedences Recorded for November 2018

Parameter	Time Period	Value of Exceedence	Date of Exceedence
NO_2 (ppm)	1 hour	-	-
CO (ppm)	8-hour rolling	-	-
PM_{10} (µg/m³)	24-hour	59.0	21/11/2018
		98.2	22/11/2018
	Annual[12]	-	-
$PM_{2.5}$ (µg/m³)	24-hour	-	-
	Annual[16]	-	-

[15] Exceedances are based on the decimal places reported.

[16] Insufficient data to report annual average, any exceedences will be reported in January 2019.

Table 14: M4 East Project Concord Oval Exceedences Recorded for November 2018

Parameter	Time Period	Value of Exceedence	Date of Exceedence
NO_2 (ppm)	1 hour	-	-
CO (ppm)	8-hour rolling	-	-
PM_{10} (µg/m³)	24-hour	59.0	21/11/2018
		92.2	22/11/2018
	Annual[13]	-	-
$PM_{2.5}$ (µg/m³)	24-hour	-	-
	Annual[17]	-	-

[17] Insufficient data to report annual average, any exceedences will be reported in January 2019.

Table 15: M4 East Project Haberfield Public School Exceedences Recorded for November 2018

Parameter	Time Period	Value of Exceedence	Date of Exceedence
NO_2 (ppm)	1 hour	-	-
CO (ppm)	8-hour rolling	-	-
PM_{10} (µg/m³)	24-hour	59.6	21/11/2018
		88.7	22/11/2018
	Annual[18]	-	-
$PM_{2.5}$ (µg/m³)	24-hour	-	-
	Annual[14]	-	-

[18] Insufficient data to report annual average, any exceedences will be reported in January 2019.

Table 16: M4 East Project Powells Creek Exceedences Recorded for November 2018

Parameter	Time Period	Value of Exceedence	Date of Exceedence
NO_2 (ppm)	1 hour	-	-
CO (ppm)	8-hour rolling	-	-
PM_{10} (µg/m³)	24-hour	68.4	21/11/2018
		111.3	22/11/2018
	Annual[15]	-	-
$PM_{2.5}$ (µg/m³)	24-hour	-	-
	Annual[19]	-	-

[19] Insufficient data to report annual average, any exceedences will be reported in January 2019.

Table 17: M4 East Project Ramsay Street Exceedences Recorded for November 2018

Parameter	Time Period	Value of Exceedence	Date of Exceedence
NO_2 (ppm)	1 hour	-	-
CO (ppm)	8-hour rolling	-	-
PM_{10} (µg/m³)	24-hour	66.1	21/11/2018
		100.3	22/11/2018
	Annual[20]	-	-
$PM_{2.5}$ (µg/m³)	24-hour	-	-
	Annual[16]	-	-

[20] Insufficient data to report annual average, any exceedences will be reported in January 2019.

Table 18: M4 East Project Saint Lukes Park Exceedences Recorded for November 2018

Parameter	Time Period	Value of Exceedence	Date of Exceedence
NO_2 (ppm)	1 hour	-	-
CO (ppm)	8-hour rolling	-	-
PM_{10} (µg/m³)	24-hour	58.2	21/11/2018
		86.6	22/11/2018
	Annual[17]	-	-
$PM_{2.5}$ (µg/m³)	24-hour	-	-
	Annual[21]	-	-

[21] Insufficient data to report annual average, any exceedences will be reported in January 2019.

5.3. Tabulated data

5.3.1. Annual average

Table 19 displays monthly averages of the $PM_{2.5}$ and PM_{10} parameters collected at M4 East project ambient air monitoring stations data from the start of monitoring (22nd December 2017) to the end current reported month. Table requires at least 75% valid data to display a monthly average. Footer values are based on all available data rather than the average of individual months. This gives an indication of performance against the annual objectives. These figures should not be considered valid until 12 months monitoring have been completed.

Table 19: 12 months to date averages of PM_{10} and $PM_{2.5}$ at the WestConnex M4 ambient air monitoring station[22]

Month	Allen Street		Concord Oval		Haberfield school		Powells Creek		Ramsay Street		Saint Lukes Park	
	PM_{10} (µg/m³)	$PM_{2.5}$ (µg/m³)	PM_{10} (µg/m³)	$PM_{2.5}$ (µg/m³)	PM_{10} (µg/m³)	$PM_{2.5}$ (µg/m³)	PM_{10} (µg/m³)	$PM_{2.5}$ (µg/m³)	PM_{10} (µg/m³)	$PM_{2.5}$ (µg/m³)	PM_{10} (µg/m³)	$PM_{2.5}$ (µg/m³)
Dec/17[23]	-	-	-	-	-	-	-	-	-	-	-	-
Jan/18	19.9	8	25.4	9	20.1	9	25.5	10	21.8	9	20.0	7
Feb/18	19.0	5	24.1	8	19.9	10	24.1	9	22.0	9	19.5	7
Mar/18	23.9	7	26.8	8	22.0	13	26.6	10	26.0	10	22.0	8
Apr/18	24.1	10	26.3	10	22.3	11	27.0	12	25.7	12	22.7	10
May/18	24.2	12	25.7	13	22.5	14	31.5	14	27.7	17	20.9	14
Jun/18	16.4	9	17.7	9	15.7	10	23.0	9	17.9	13	14.3	11
Jul/18	22.9	11	24.9	10	21.3	12	30.7	12	29.1	16	19.6	13
Aug/18	22.3	9	21.1	9	20.5	11	25.2	10	24.3	14	18.0	11
Sep/18	18.2	8	19.4	7	18.1	10	21.9	9	20.4	11	16.9	9
Oct/18	17.3	6	18.4	5	16.4	8	20.3	7	18.5	9	15.3	8
Nov/18	24.1	7	24.2	7	23.9	-	28.3	9	29.2	10	21.9	9
Average	**21.1**	**8.4**	**23.0**	**8.6**	**20.2**	**10.9**	**25.8**	**10.2**	**23.8**	**11.8**	**19.2**	**9.9**

[22] Note: data collection commenced in December 2017; therefore, 12 consecutive months of data have not yet been recorded.

[23] Less than 75% data available for December 2017

5.4. Graphic Representations

This section displays graphs of the pollutants and meteorological parameters monitored at the M4 East sites for November 2018. The graphs are based on validated 5 minutes or 1-hour data as appropriate.

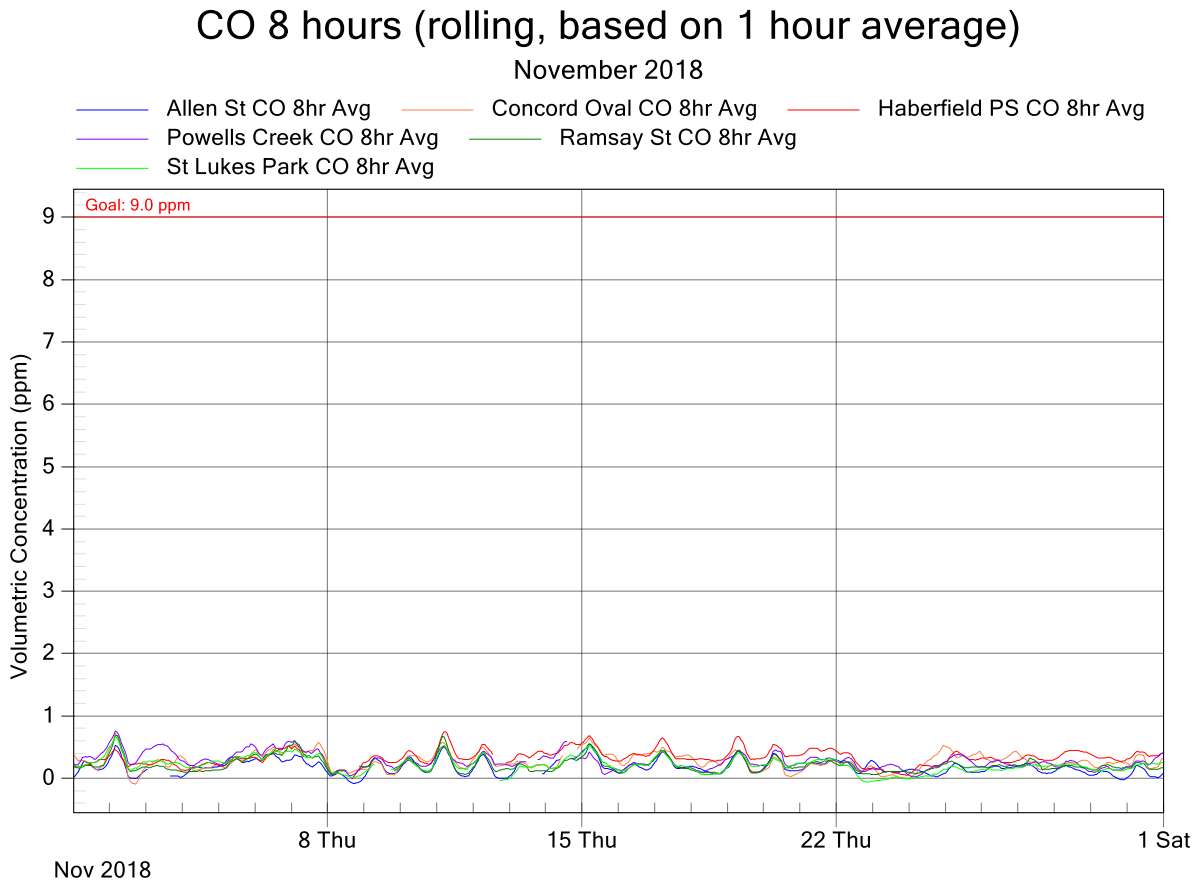

Figure 2: M4 East Project Air Monitoring Stations - CO 8 hours Rolling graph for November 2018

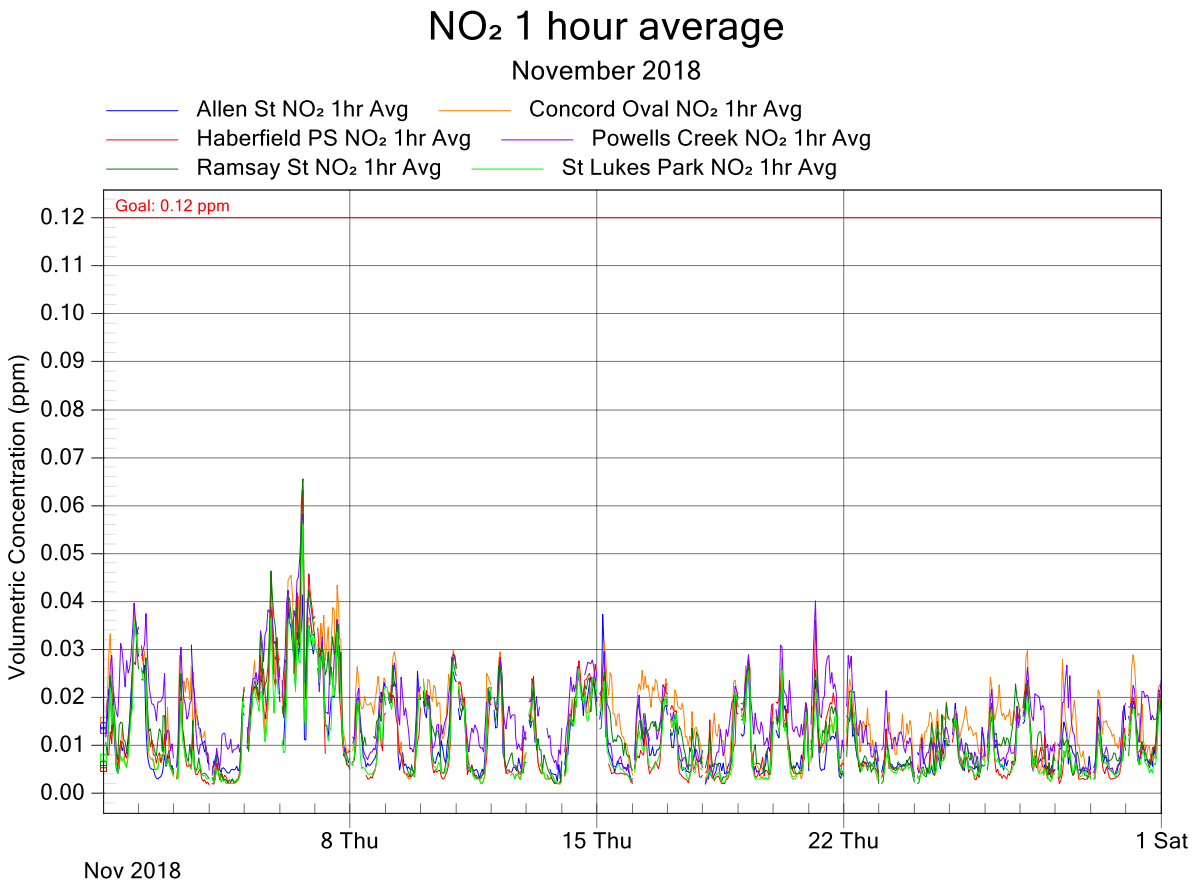

Figure 3: M4 East Project Air Monitoring Stations - NO_2 graph for November 2018

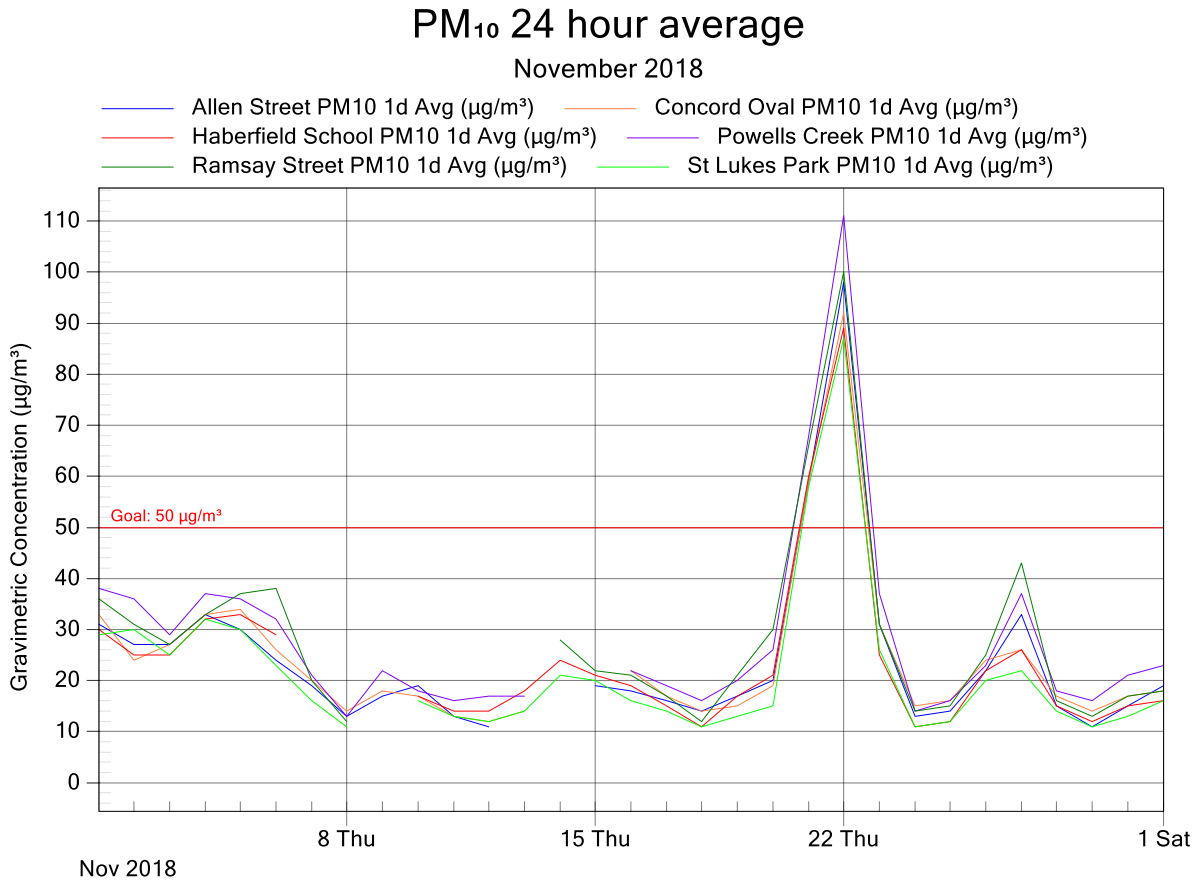

Figure 4: M4 East Project Air Monitoring Stations - PM_{10} 24 Hour graph for November 2018

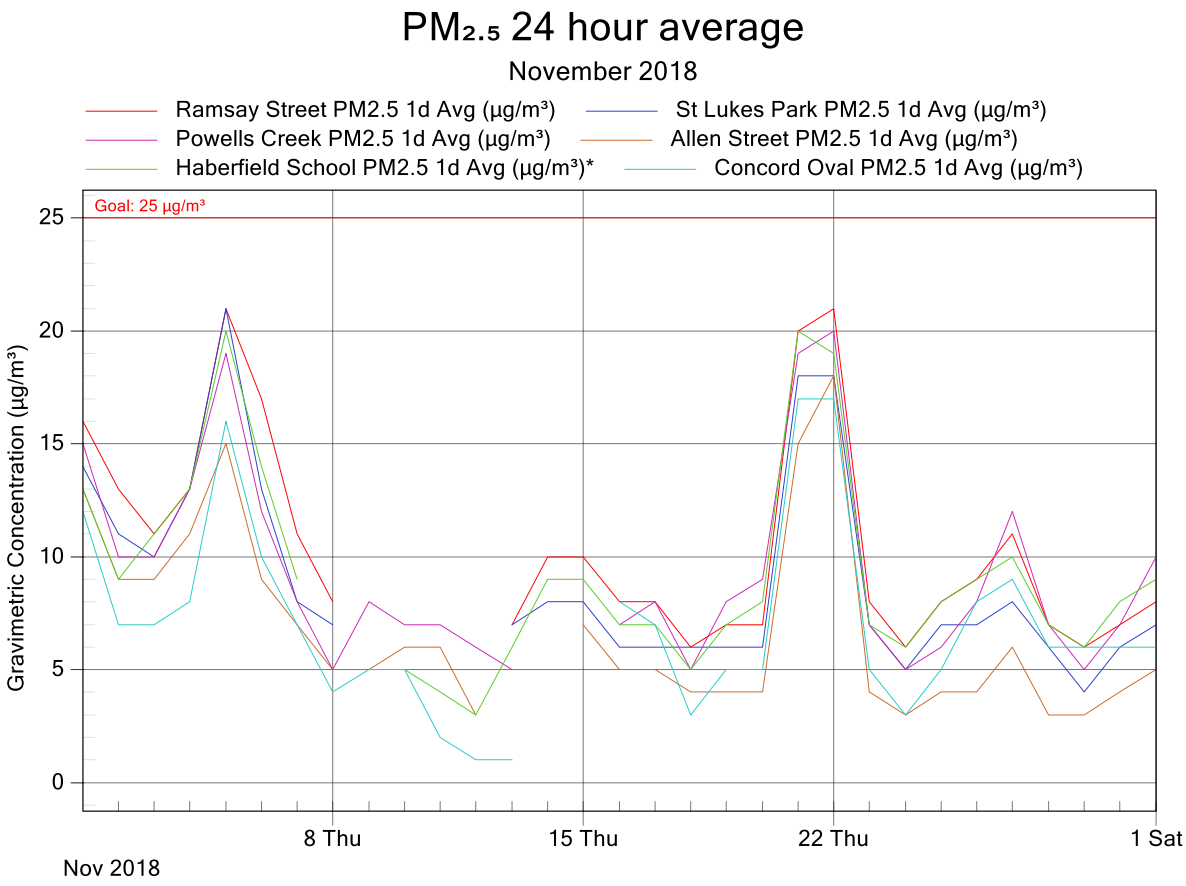

Figure 5: M4 East Project Air Monitoring Stations - $PM_{2.5}$ 24 Hour graph November 2018

*Data for Haberfield School station has been included in this figure for reference purposes only. Refer to Appendix 3 for details.

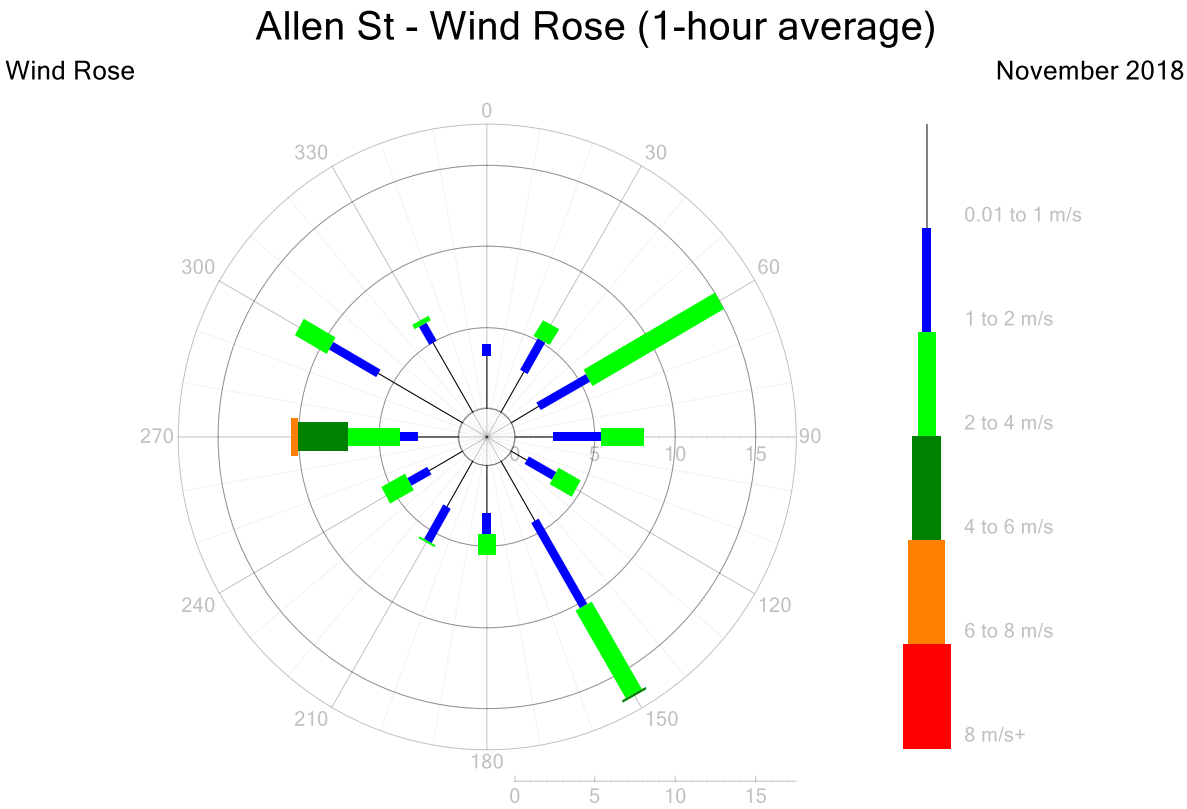

Figure 6: Allen Street – Wind Rose for November 2018

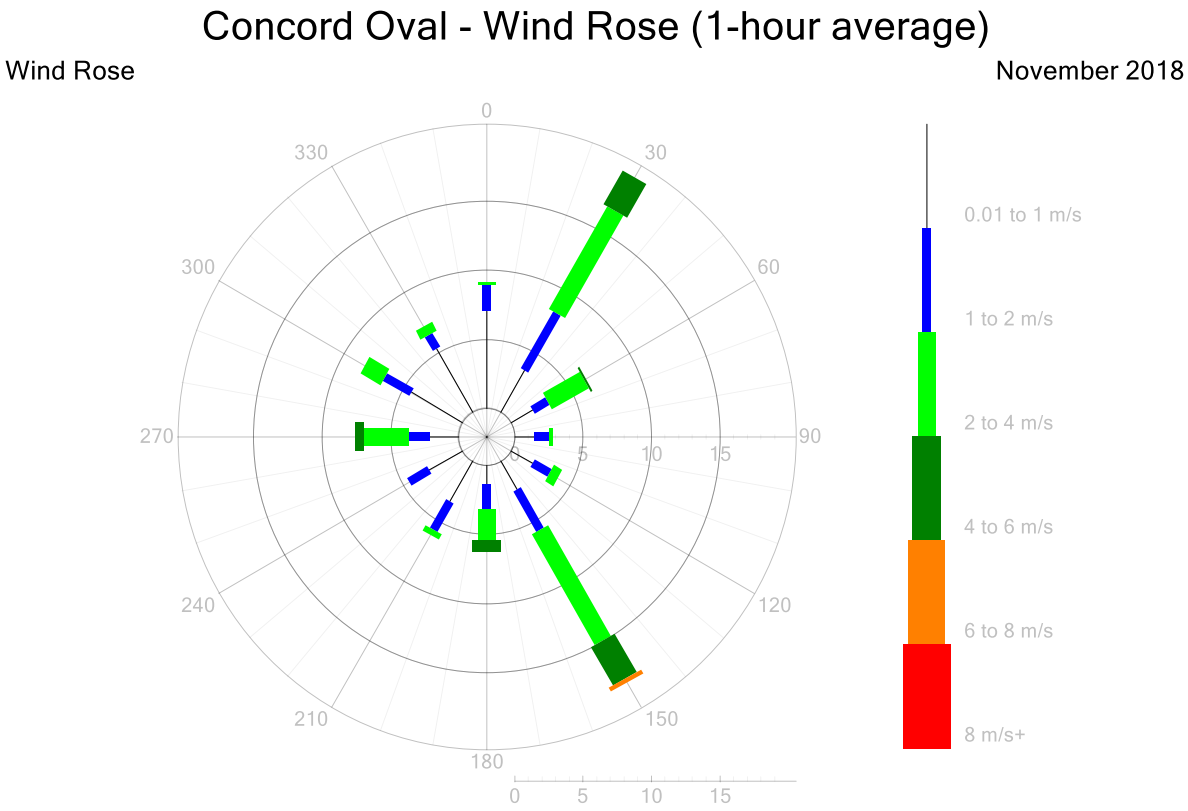

0.1% calm
99.4% valid data present

Figure 7: Concord Oval – Wind Rose for November 2018

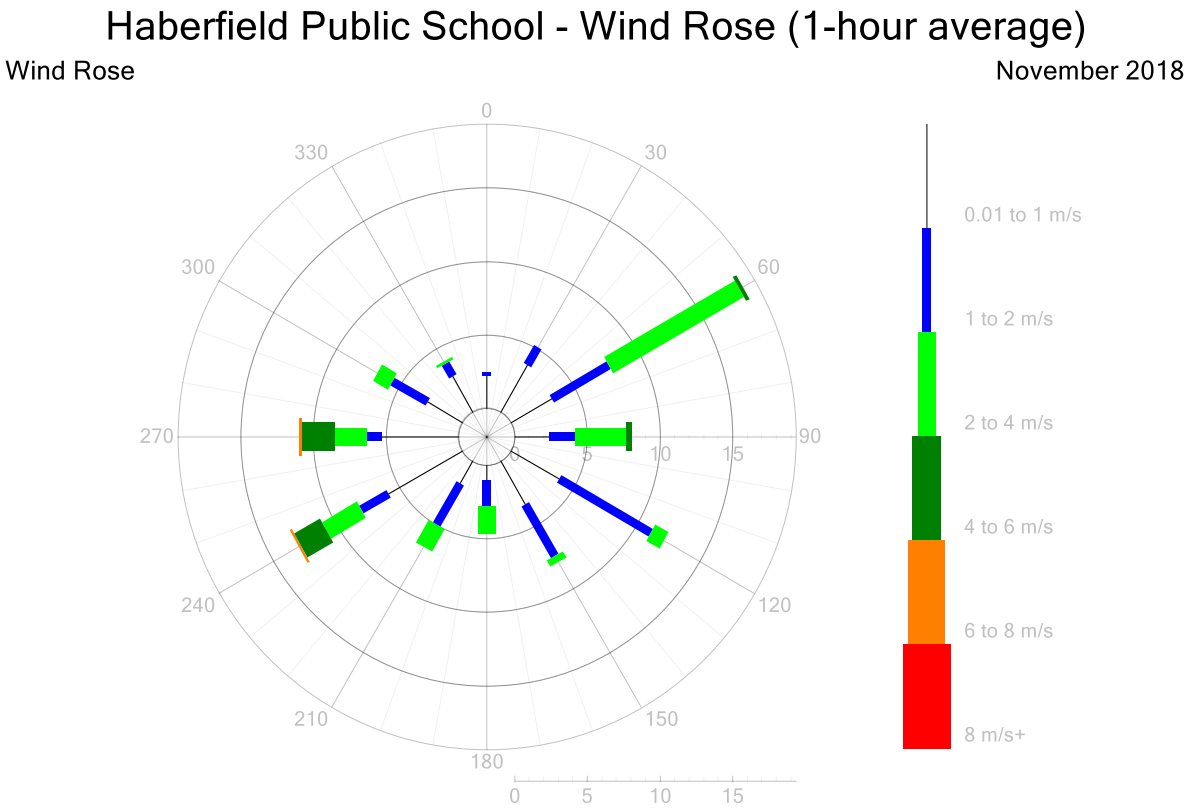

0.0% calm
95.1% valid data present

Figure 8: Haberfield Public School – Wind Rose for November 2018

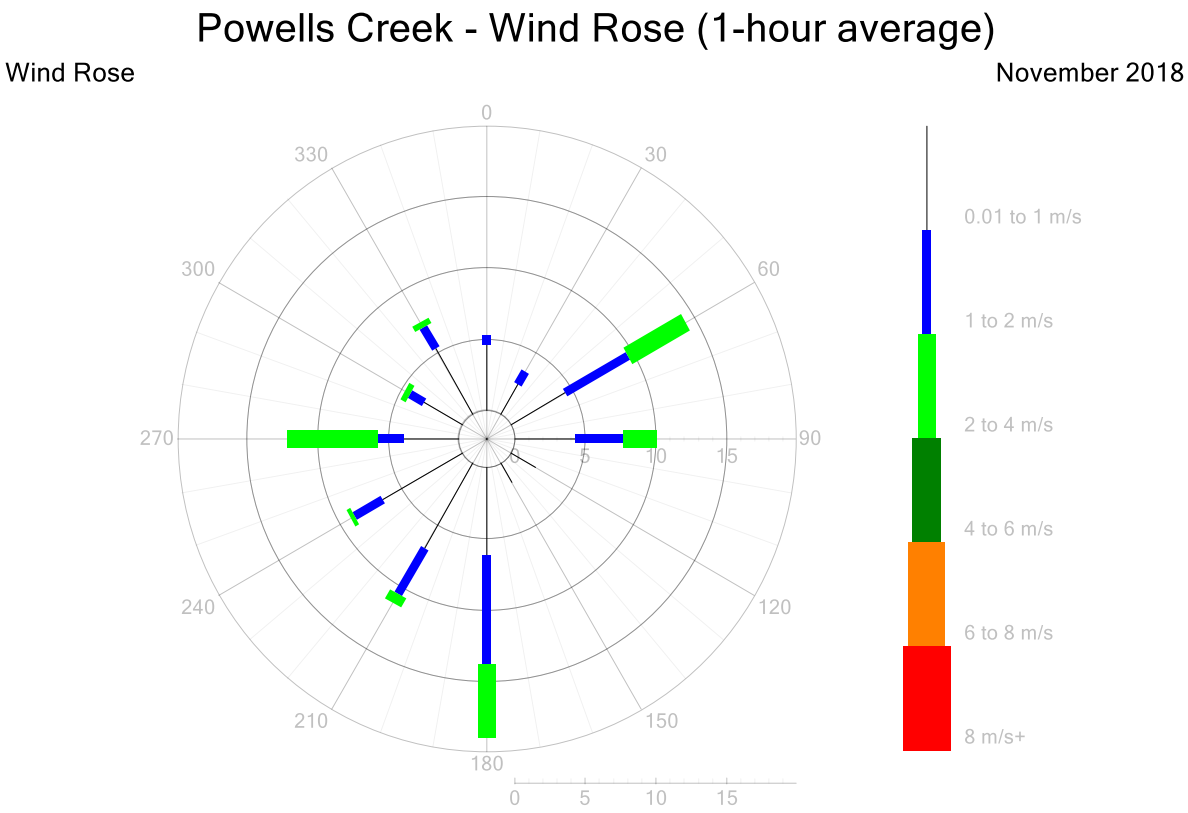

0.0% calm
97.6% valid data present

Figure 9: Powells Creek – Wind Rose for November 2018

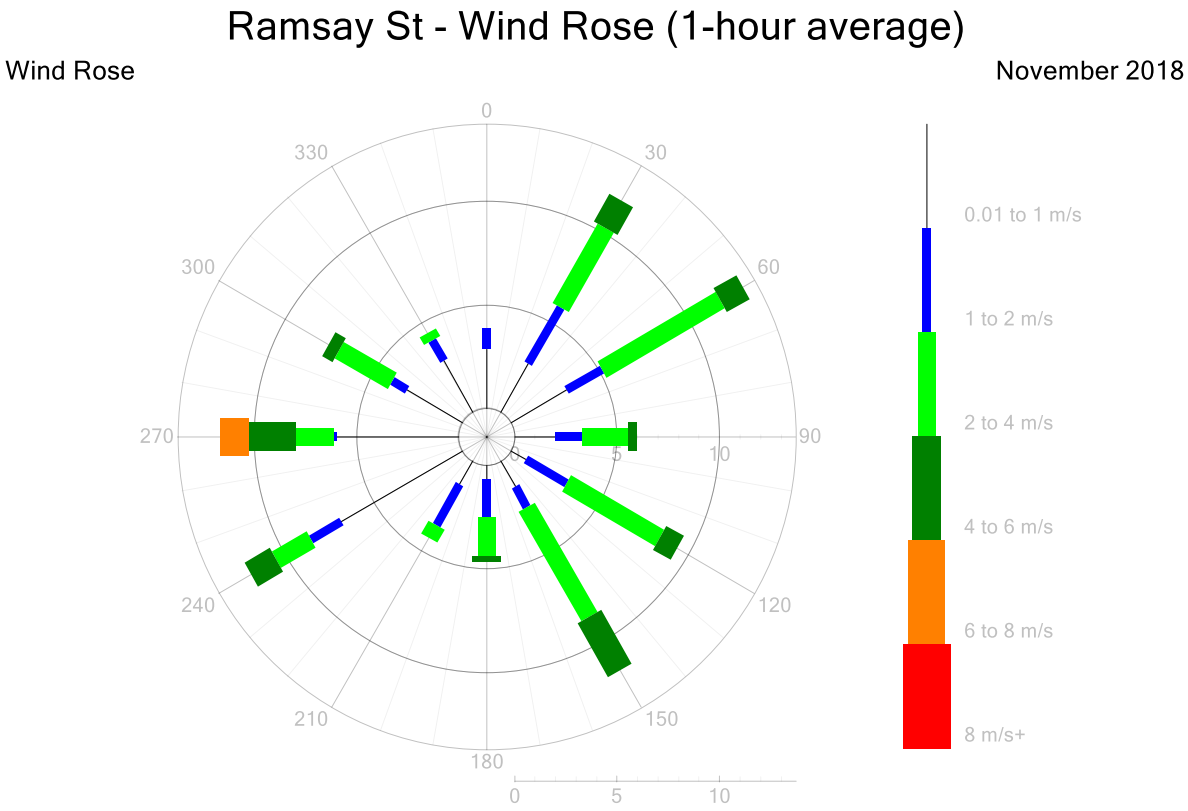

0.0% calm
97.9% valid data present

Figure 10: Ramsay Street – Wind Rose for November 2018

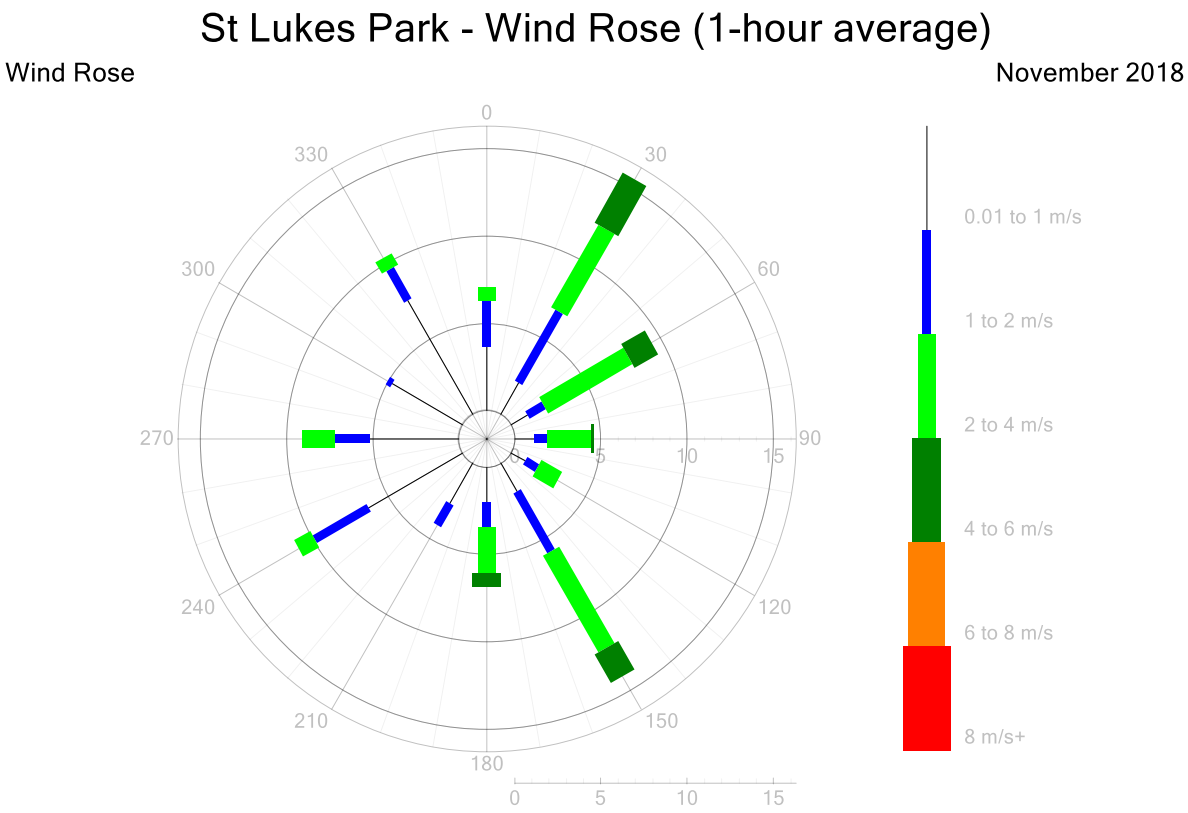

0.0% calm
88.8% valid data present

Figure 11: Saint Lukes Park – Wind Rose for November 2018

6.0 Valid Data Exception Tables

Tables 20 to 25 below detail all changes made to the raw data set during the validation process. An explanation of reasons given in the table can be found in Appendix 2.

Table 20: Allen Street Valid Data Exception Table

Start Date	End Date	Reason	Change Details	User Name	Change Date
01/11/18 00:00	13/11/18 06:40	Instrument failed its "as found" calibration and required an offset adjustment. A step change can be observed on October 2nd and data has been invalidated back to this point. A correction could not be applied as the offset was not consistent throughout this period.	AT 10m	AA	7/12/2018
01/11/18 01:00	30/11/18 01:25	Automatic span and zero checks once daily for 30 minutes	CO, NO, NO_2, NO_X	AA	7/12/2018
01/11/18 13:45	30/11/18 02:00	Intermittent data transmission errors	CO, NO, NO_2, NO_X, PM_{10}, AT 2m, AT 10m, WS, WD, Sigma	AA	7/12/2018
01/11/18 13:55	27/11/18 19:55	Intermittent additional background checks	CO	AA	7/12/2018
01/11/18 23:45	30/11/18 23:50	Background checks once daily for 5 - 10 minutes	CO	AA	7/12/2018
01/11/18 23:50	02/11/18 23:40	Linear offset of A=0ppm and B=0.3ppm applied to correct baseline drift	CO	AA	7/12/2018
03/11/18 01:25	03/11/18 10:45	Instrument fault - instrument stuck in calibration mode	CO, NO, NO_2, NO_X	AA	7/12/2018
03/11/18 10:50	03/11/18 11:25	Logger restarted followed by instrument stabilisation - Instrument fault fixed	CO, NO, NO_2, NO_X, PM_{10}, AT 2m, AT 10m, WS, WD, Sigma	AA	7/12/2018
03/11/18 23:55	04/11/18 23:40	Linear offset of A=0ppm and B=0.195ppm applied to correct baseline drift	CO	AA	7/12/2018
07/11/18 19:15	07/11/18 19:55	Unrealistic negative readings	PM_{10}	AA	7/12/2018
13/11/18 06:00	13/11/18 16:10	Scheduled yearly maintenance commenced. Zero filter installed	All parameters	AA	7/12/2018

Start Date	End Date	Reason	Change Details	User Name	Change Date
13/11/18 16:10	14/11/18 08:00	Zero check running for BAM and TEOM	PM_{10}, $PM_{2.5}$	AA	7/12/2018
14/11/18 08:05	14/11/18 12:00	Scheduled yearly maintenance followed by instrument stabilisation - zero filter removed	All parameters	AA	7/12/2018
16/11/18 23:50	17/11/18 23:40	Linear offset of A=0.130ppm and B=0.270ppm applied to correct baseline drift	CO	AA	7/12/2018
17/11/18 23:55	18/11/18 23:40	Linear offset of A=0.100ppm and B=0.270ppm applied to correct baseline drift	CO	AA	7/12/2018
20/11/18 23:50	21/11/18 23:40	Linear offset of A=0.000ppm and B=0.327ppm applied to correct baseline drift	CO	AA	7/12/2018
25/11/18 23:50	26/11/18 23:40	Linear offset of A=0.000ppm and B=0.240ppm applied to correct baseline drift	CO	AA	7/12/2018

Table 21: Concord Oval Valid Data Exception Table

Start Date	End Date	Reason	Change Details	User Name	Change Date
01/11/18 01:00	30/11/18 01:25	Automatic span and zero checks once daily for 30 - 35 minutes	CO, NO, NO_2, NO_x	AA	11/12/2018
01/11/18 12:50	30/11/18 17:30	Intermittent data transmission errors	CO, NO, NO_2, NO_x	AA	11/12/2018
01/11/18 23:45	30/11/18 23:45	Background checks once daily for 5 - 15 minutes	CO	AA	11/12/2018
06/11/18 17:05	07/11/18 19:55	Unrealistic negative readings	PM_{10}	AA	11/12/2018
14/11/18 09:00	14/11/18 15:10	Scheduled yearly maintenance commenced. Zero filter installed	All parameters	AA	11/12/2018
14/11/18 15:00	15/11/18 07:50	Zero check running for BAM and TEOM	PM_{10}, $PM_{2.5}$	AA	11/12/2018
15/11/18 07:55	15/11/18 08:25	Scheduled yearly maintenance followed by instrument stabilisation - zero filter removed	PM_{10}, $PM_{2.5}$	AA	11/12/2018
19/11/18 13:40	19/11/18 15:00	Scheduled yearly maintenance performed - Ambient temperature sensors yearly calibration	AT 2m, AT 10m	AA	11/12/2018
29/11/18 12:45	29/11/18 12:45	Unrealistic negative readings	NO, NO_2, NO_x	AA	11/12/2018

Table 22: Haberfield Public School Valid Data Exception Table

Start Date	End Date	Reason	Change Details	User Name	Change Date
01/11/18 01:00	30/11/18 01:25	Automatic span and zero checks once daily for 30 minutes	CO, NO, NO_2, NO_x	AA	11/12/2018
01/11/18 02:30	30/11/18 21:25	Intermittent data transmission errors	CO, NO, NO_2, NO_x, AT2m, AT10m, WS, WD, Sigma, PM_{10}	AA	11/12/2018
01/11/18 23:40	30/11/18 23:45	Background checks once daily for 5 - 10 minutes	CO	AA	11/12/2018
06/11/18 17:15	27/11/18 14:45	Intermittent unrealistic negative readings	PM_{10}	AA	11/12/2018
07/11/18 08:00	07/11/18 14:30	Scheduled yearly maintenance commenced	All parameters	AA	11/12/2018
07/11/18 14:30	07/11/18 23:40	Linear offset of A=0ppm and B= -0.397ppm applied to correct span drift	CO	AA	11/12/2018
08/11/18 07:00	08/11/18 11:05	Scheduled yearly maintenance continued - Zero filter installed	All parameters	AA	11/12/2018
08/11/18 11:10	09/11/18 10:55	Zero check running for BAM and TEOM	PM_{10}, $PM_{2.5}$	AA	11/12/2018
08/11/18 16:30	08/11/18 16:35	Additional background check following maintenance	CO	AA	11/12/2018
09/11/18 11:00	09/11/18 12:55	Scheduled yearly maintenance completed followed by instrument stabilisation- zero filter removed	PM_{10}, $PM_{2.5}$	AA	11/12/2018
09/11/18 12:00	01/12/18 00:00	Data does not meet traceability requirements of AS/NZS 3580.9.12-2013 and has been deemed as invalid	$PM_{2.5}$	AA	17/05/2019
12/11/18 12:00	12/11/18 16:00	Non-scheduled maintenance performed followed by instrument stabilisation-Gas diluter / Serical unit swapped out (IN: 17-1738, OUT: 17-1305)	CO, NO, NO_2, NO_x, AT2m, AT10m, WS, WD, Sigma, PM_{10}	AA	11/12/2018
12/11/18 16:05	13/11/18 11:50	Instrument fault - data not available	WS, WD, Sigma	AA	11/12/2018

Start Date	End Date	Reason	Change Details	User Name	Change Date
13/11/18 12:00	13/11/18 13:15	Non-scheduled maintenance performed - Instrument fault fixed	CO, NO, NO_2, NO_x, AT2m, AT10m, WS, WD, Sigma, PM_{10}	AA	11/12/2018
19/11/18 07:45	19/11/18 09:55	Scheduled yearly maintenance performed - Ambient temperature sensors yearly calibration	AT 2m, AT 10m	AA	11/12/2018
23/11/18 01:30	23/11/18 23:40	Static offset of -0.822ppm applied to correct baseline drift	CO	AA	11/12/2018

Table 23: Powells Creek Valid Data Exception Table

Start Date	End Date	Reason	Change Details	User Name	Change Date
01/11/18 01:00	30/11/18 01:25	Automatic span and zero check, once daily for 30 minutes	CO, NO, NO_2, NO_X	AA	12/12/2018
01/11/18 12:35	22/11/18 13:10	Intermittent additional background checks	CO	AA	12/12/2018
01/11/18 15:25	30/11/18 15:30	Background checks, once daily for 10 minutes	CO	AA	12/12/2018
01/11/18 20:00	27/11/18 21:25	Intermittent data transmission errors	CO, NO, NO_2, NO_X	AA	12/12/2018
07/11/18 19:20	07/11/18 19:55	Unrealistic negative readings	PM_{10}	AA	12/12/2018
08/11/18 13:55	29/11/18 17:20	Intermittent unrealistic negative readings	NO, NO_2, NO_X	AA	12/12/2018
13/11/18 10:00	13/11/18 13:20	Scheduled yearly maintenance commenced, followed by instrument stabilisation	All parameters	AA	12/12/2018
14/11/18 13:00	14/11/18 15:55	Scheduled yearly maintenance continued - Zero filter installed	All parameters	AA	12/12/2018
14/11/18 16:00	15/11/18 06:55	Zero check running for BAM and TEOM	PM_{10}, $PM_{2.5}$	AA	12/12/2018
15/11/18 02:25	16/11/18 13:35	Intermittent suspected brief power interruptions	CO, NO, NO_2, NO_X, AT 2m, AT 10m, WS, WD, Sigma, PM_{10}	AA	12/12/2018
15/11/18 07:00	15/11/18 08:50	Scheduled yearly maintenance completed followed by instrument stabilisation- zero filter removed	PM_{10}, $PM_{2.5}$	AA	12/12/2018
20/11/18 10:30	20/11/18 12:25	Scheduled yearly maintenance performed - Ambient temperature sensors yearly calibration	AT 2m, AT 10m	AA	12/12/2018
28/11/18 04:00	29/11/18 08:50	Instrument fault - unrealistic readings not tracking with other sites	AT 2m, AT 10m	AA	12/12/2018
28/11/18 04:45	28/11/18 14:05	Instrument fault - unrealistic readings	WS, WD, Sigma	AA	12/12/2018

Table 24: Ramsay Street Valid Data Exception Table

Start Date	End Date	Reason	Change Details	User Name	Change Date
01/11/18 01:00	30/11/18 01:40	Automatic span and zero checks, once daily for 40 - 45 minutes	CO, NO, NO_2, NO_X	AA	12/12/2018
01/11/18 02:00	30/11/18 14:35	Intermittent data transmission errors	CO, NO, NO_2, NO_X, WS, WD, Sigma, AT 2m, AT 10m, PM_{10}	AA	12/12/2018
01/11/18 23:50	30/11/18 23:50	Background checks, once daily for 5 - 10 minutes	CO	AA	12/12/2018
06/11/18 17:15	07/11/18 20:00	Intermittent unrealistic negative readings	PM_{10}	AA	12/12/2018
08/11/18 11:00	08/11/18 15:55	Scheduled yearly maintenance commenced, followed by instrument stabilisation	All parameters	AA	12/12/2018
09/11/18 07:00	09/11/18 14:25	Scheduled yearly maintenance continued, followed by instrument stabilisation - Zero filter installed	All parameters	AA	12/12/2018
09/11/18 14:30	12/11/18 07:55	Zero check running for BAM and TEOM	PM_{10}, $PM_{2.5}$	AA	12/12/2018
12/11/18 08:00	12/11/18 16:00	Scheduled yearly maintenance continued, followed by instrument stabilisation- zero filter removed. TEOM instrument swap out (IN: 04-1050, OUT: 17-2481) - Zero filter installed	WS, WD, Sigma, PM_{10}, $PM_{2.5}$	AA	12/12/2018
12/11/18 16:05	13/11/18 07:35	Zero check running for TEOM (ID: 04-1050)	PM_{10}	AA	12/12/2018
13/11/18 07:40	13/11/18 07:40	Scheduled yearly maintenance completed - Zero filter removed	PM_{10}	AA	12/12/2018
16/11/18 15:00	18/11/18 08:00	Intermittent beta data gaps manually filled up according to the hourly readings	$PM_{2.5}$	AA	12/12/2018
19/11/18 10:30	19/11/18 12:10	Scheduled yearly maintenance performed - Ambient temperature sensors yearly calibration	AT 2m, AT 10m	AA	12/12/2018
19/11/18 16:45	30/11/18 20:40	Intermittent additional background checks	CO	AA	12/12/2018
22/11/18 11:00	22/11/18 11:00	Unrealistic negative readings	NO, NO_2, NO_X	AA	12/12/2018

Table 25: Saint Lukes Park Valid Data Exception Table

Start Date	End Date	Reason	Change Details	User Name	Change Date
01/11/18 01:00	30/11/18 01:40	Automatic span and zero checks, once daily for 25 - 50 minutes	CO, NO, NO_2, NO_x	AA	12/12/2018
01/11/18 16:20	27/11/18 18:05	Intermittent power interruptions followed by instrument stabilisation	All parameters	AA	12/12/2018
01/11/18 21:40	30/11/18 15:40	Intermittent data transmission errors	WS, WD, Sigma, AT 2m, AT 10m, PM_{10}, NO, NO_2, NO_x	AA	12/12/2018
01/11/18 23:45	30/11/18 23:50	Background checks, once daily for 5 - 15 minutes	CO	AA	12/12/2018
02/11/18 13:05	02/11/18 15:15	Scheduled yearly maintenance commenced - Meteorological instruments	WS, WD, Sigma, AT 2m, AT 10m	AA	12/12/2018
02/11/18 13:20	02/11/18 16:05	Intermittent additional background checks	CO	AA	12/12/2018
06/11/18 12:10	09/11/18 06:00	Logger fault - Only CO, NO, NO_2, NO_x, PM_{10} and $PM_{2.5}$ data was recoverable directly from the instruments	WS, WD, Sigma, AT 10m, AT 2m	AA	12/12/2018
06/11/18 17:10	07/11/18 19:55	Intermittent unrealistic negative readings	PM_{10}	AA	12/12/2018
09/11/18 06:00	09/11/18 15:45	Scheduled yearly maintenance continued, followed by instrument stabilisation	All parameters	AA	12/12/2018
09/11/18 15:00	12/11/18 06:00	Zero check running for BAM	$PM_{2.5}$	AA	12/12/2018
12/11/18 07:00	12/11/18 12:45	Scheduled yearly maintenance continued - Zero filter removed	All parameters	AA	12/12/2018
20/11/18 08:05	20/11/18 09:45	Scheduled yearly maintenance completed - Ambient temperature sensors yearly calibration	AT 2m, AT 10m	AA	12/12/2018

7.0 Report Summary

- Percentage availability for some parameters at M4 East Project was below 95%, refer to Table 12, and Tables 20-25 for details.
- There two exceedances of the air quality limits at the M4 East Westconnex Ambient Air Quality Monitoring Network for the reporting month. Please refer to Table 13-18 in Section 5.2 – Air Quality Monthly Summary for further information. Ecotech have been advised that Sydney had experienced elevated particulate levels due to dust storms which may have had significant impact on reported particulate concentrations during 21st to 22nd November 2018.

Appendix 1 - Definitions & Abbreviations

ERS	Environmental Reporting Services
AQMS	Air Quality Monitoring Station
AQM	Air Quality Monitor
BAM	Beta Attenuation Monitors
TEOM	Tapered Element Oscillating Microbalance
°	Degrees (True North)
K	Kelvin
µg/m³	Micrograms per cubic metre at standard temperature and pressure (0°C and 101.3 kPa)
AT	Ambient Temperature
calm	Wind conditions where the wind speed is below the operating range of the wind sensor
CO	Carbon monoxide
mg/m^3	Milligrams per cubic metre at standard temperature and pressure (0°C and 101.3 kPa)
mm	Millimeters
NO	Nitric oxide
NO_2	Nitrogen dioxide
NO_x	Oxides of nitrogen
PM_{10}	Particulate less than 10 microns in equivalent aerodynamic diameter
$PM_{2.5}$	Particulate less than 2.5 microns in equivalent aerodynamic diameter
ppb	Parts per billion

ppm	Parts per million
RH	Relative Humidity
WD	Vector Wind Direction
WS	Vector Wind Speed

Appendix 2 - Explanation of Exception Table

Automatic filter tape advance refers to the movement of the filter paper by the analyser to an un-used spot.

Automatic background check refers to when analyser samples zero air and measures the level of the concentration voltage. This voltage is taken as the zero signal level and this value is subtracted from any subsequent readings as an active zero compensation. This is the analyser's fine zero measurement.

Automatic span/zero check. The E-Sampler is programmed to perform a zero calibration check whereby air is passed through filter element, removing particulates, before entering the sensor in the analyser. Data is invalidated when these checks occur.

Beta count failure refers to a fault in the functioning of the EBAM. A one minute beta count was less than the maximum acceptable counts during operation.

Calibration check outside tolerance refers to when the calibration values are outside the tolerance limits set for the precision check.

Calibration correction factor applied to data refers to an offset or multiplier applied to the data. This operation may be performed for a number of reasons including: (a) when a clear trend / drift outside the tolerance limit can be demonstrated by repeated operation precision checks, (b) when a correction is required on previously logged data due to a calibration check being outside the allowable tolerance

Commissioning refers to the initial setup and calibration of the instrument when it is first installed. For some instruments there may be a stabilisation period before normal operation commences.

Data transmission error refers to a period of time when the instrument could not transmit data. This may be due to interference, or a problem with the phone line or modem.

Equipment malfunction/instrument fault refers to a period of time when the instrument was not in the normal operating mode and did not measure a representative value of the existing conditions.

Gap in data/data not available refers to a period of time when either data has been lost or could not be collected.

Instrument Alarm refers to an alarm produced by the instrument. A range of alarms can be produced depending on how operation of the instrument is being affected.

Instrument out of service refers to a lack of data due to an instrument being shut down for repair, maintenance, or factory calibration.

Linear offset or multiplier refers to when an offset or multiplier has been applied between two points where the values of the offset or multiplier are different and the correction is interpolated between the two points.

Logger error refers to when an error occurs and instrument readings are not correctly recorded by the logger.

Maintenance refers to a period of time when the logger/instrument was switched off due to maintenance.

Overnight span/zero out of tolerance refers to when the span/zero reading measured by the analyser during an automatic precision check falls outside of the expected concentration limits.

Overnight zero out of tolerance refers to when the automatic zero reading measured by the analyser falls outside the expected limits.

Power Interruption refers to no power to the station therefore no data was collected at this time.

Remote Calibration refers to when a technician remotely connects to the station and manually performs a span check.

Static offset or multiplier refers to when a single offset or multiplier has been applied to the data between two points either to increase or decrease the measured value.

Tape break refers to the breaking of the EBAM/BAM sample tape during operation.

Warm up after power interruption refers to the startup period of an instrument after power has been restored.

Appendix 3 - Amendments

This amended report supersedes previously issued versions of the report. Refer to the revision history table on page 2 for details of previous revisions. The following modifications have been made in this version:

- Following an investigation into elevated $PM_{2.5}$ readings at Haberfield School station, data shown in figure 5 has had a correction applied based on the internal background setting observed in a visit in March 2019.

  Although this correction gives plausible $PM_{2.5}$ data that tracks closely with other sites, it was concluded that the data does not meet the traceability requirements of AS/NZS 3580.9.12-2013 due to the lack of documented evidence. $PM_{2.5}$ data for Haberfield School from 9th November 2018 at 12:00 should, therefore, be considered for reference only.

  This data has not been used to compile station statistics.

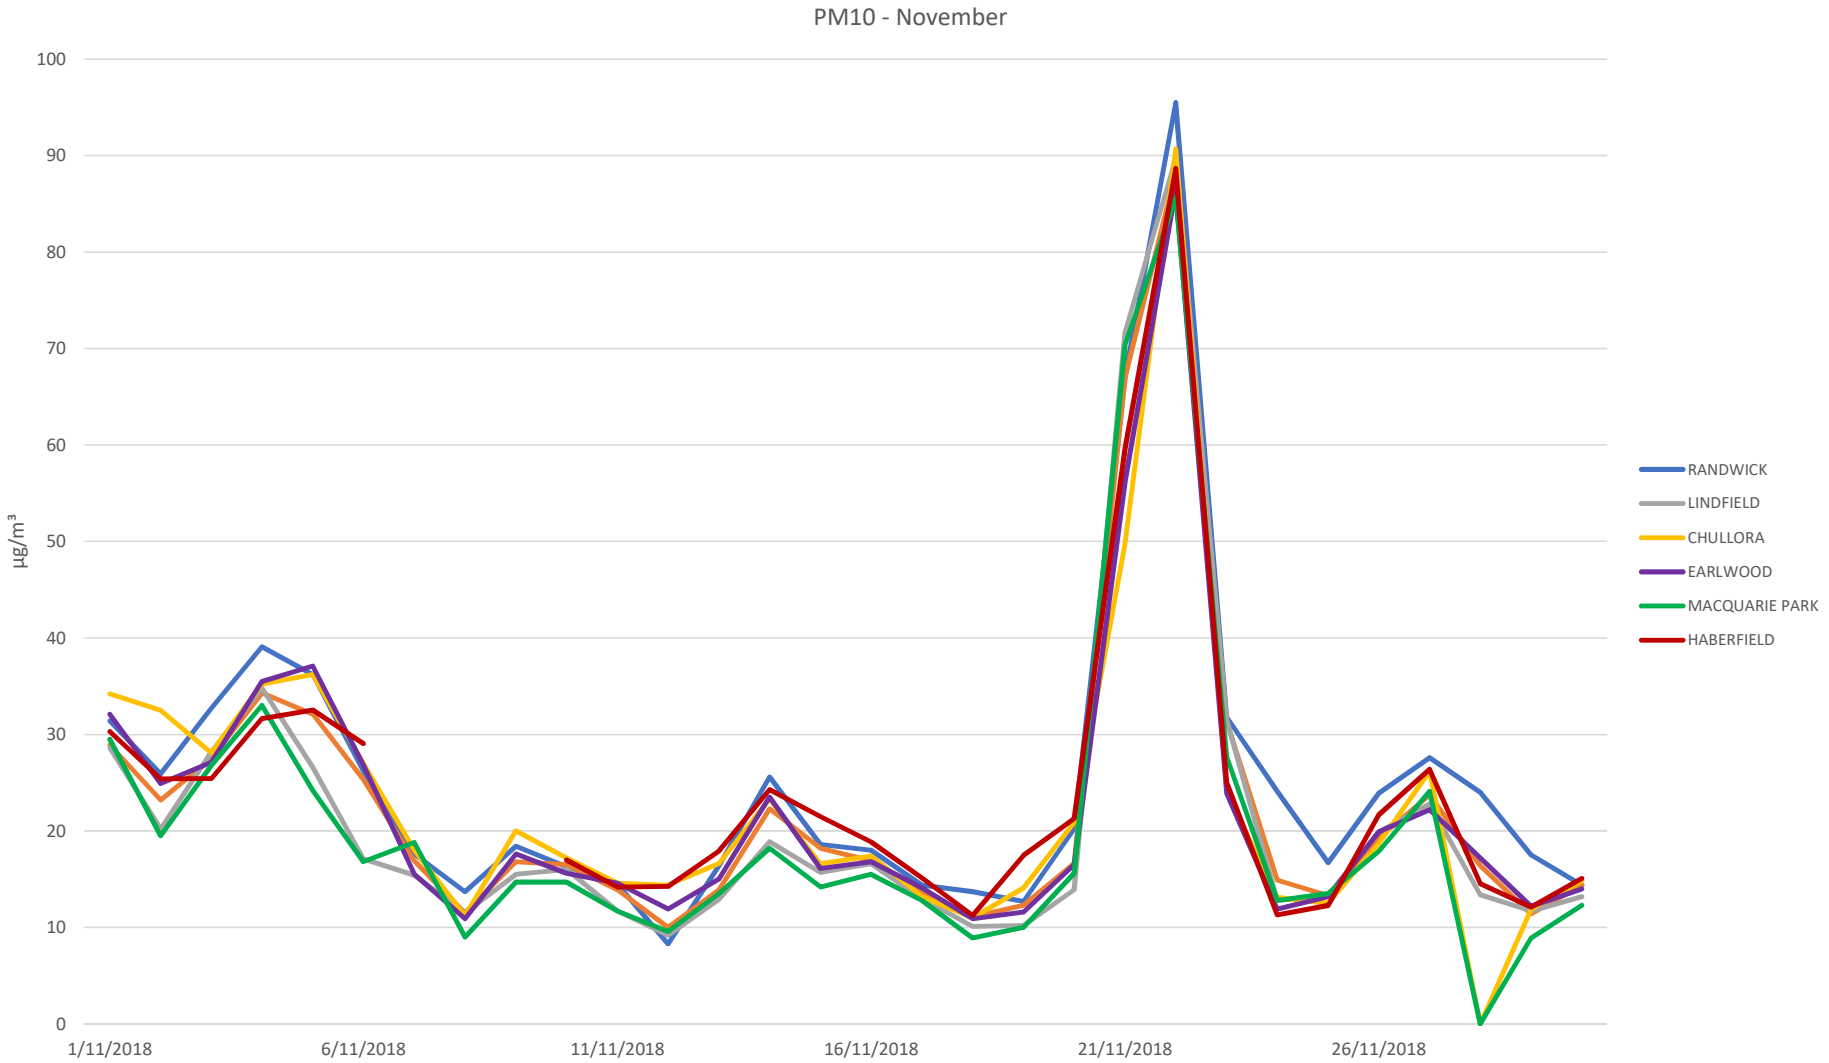
PM10 - November
µg/m³
100
90
80
70
60
50
40
30
20
10
0
1/11/2018
6/11/2018
11/11/2018
16/11/2018
21/11/2018
26/11/2018
RANDWICK
LINDFIELD
CHULLORA
EARLWOOD
MACQUARIE PARK
HABERFIELD

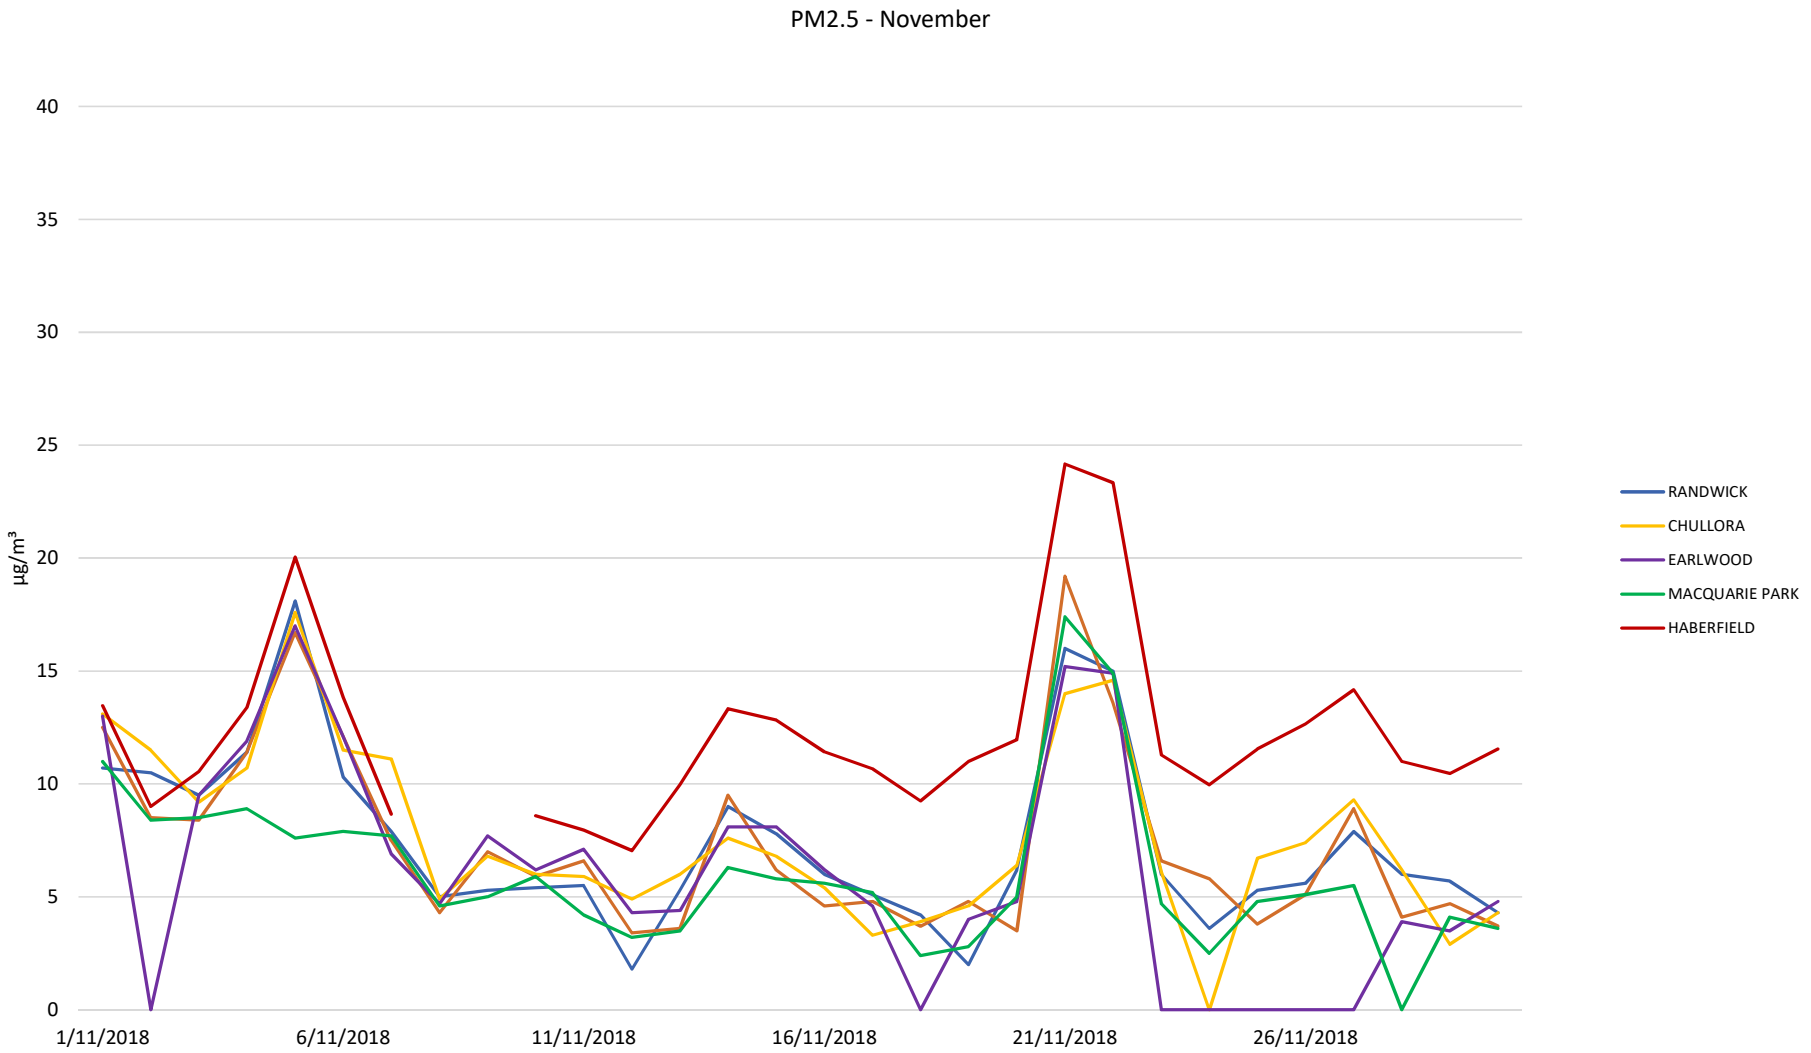
PM2.5 - November
µg/m³
40
35
30
25
20
15
10
5
0
1/11/2018
6/11/2018
11/11/2018
16/11/2018
21/11/2018
26/11/2018
RANDWICK
CHULLORA
EARLWOOD
MACQUARIE PARK
HABERFIELD
